Team 15: SpinShelf (Everyday Reach) Project Plan, Weeks 10-14

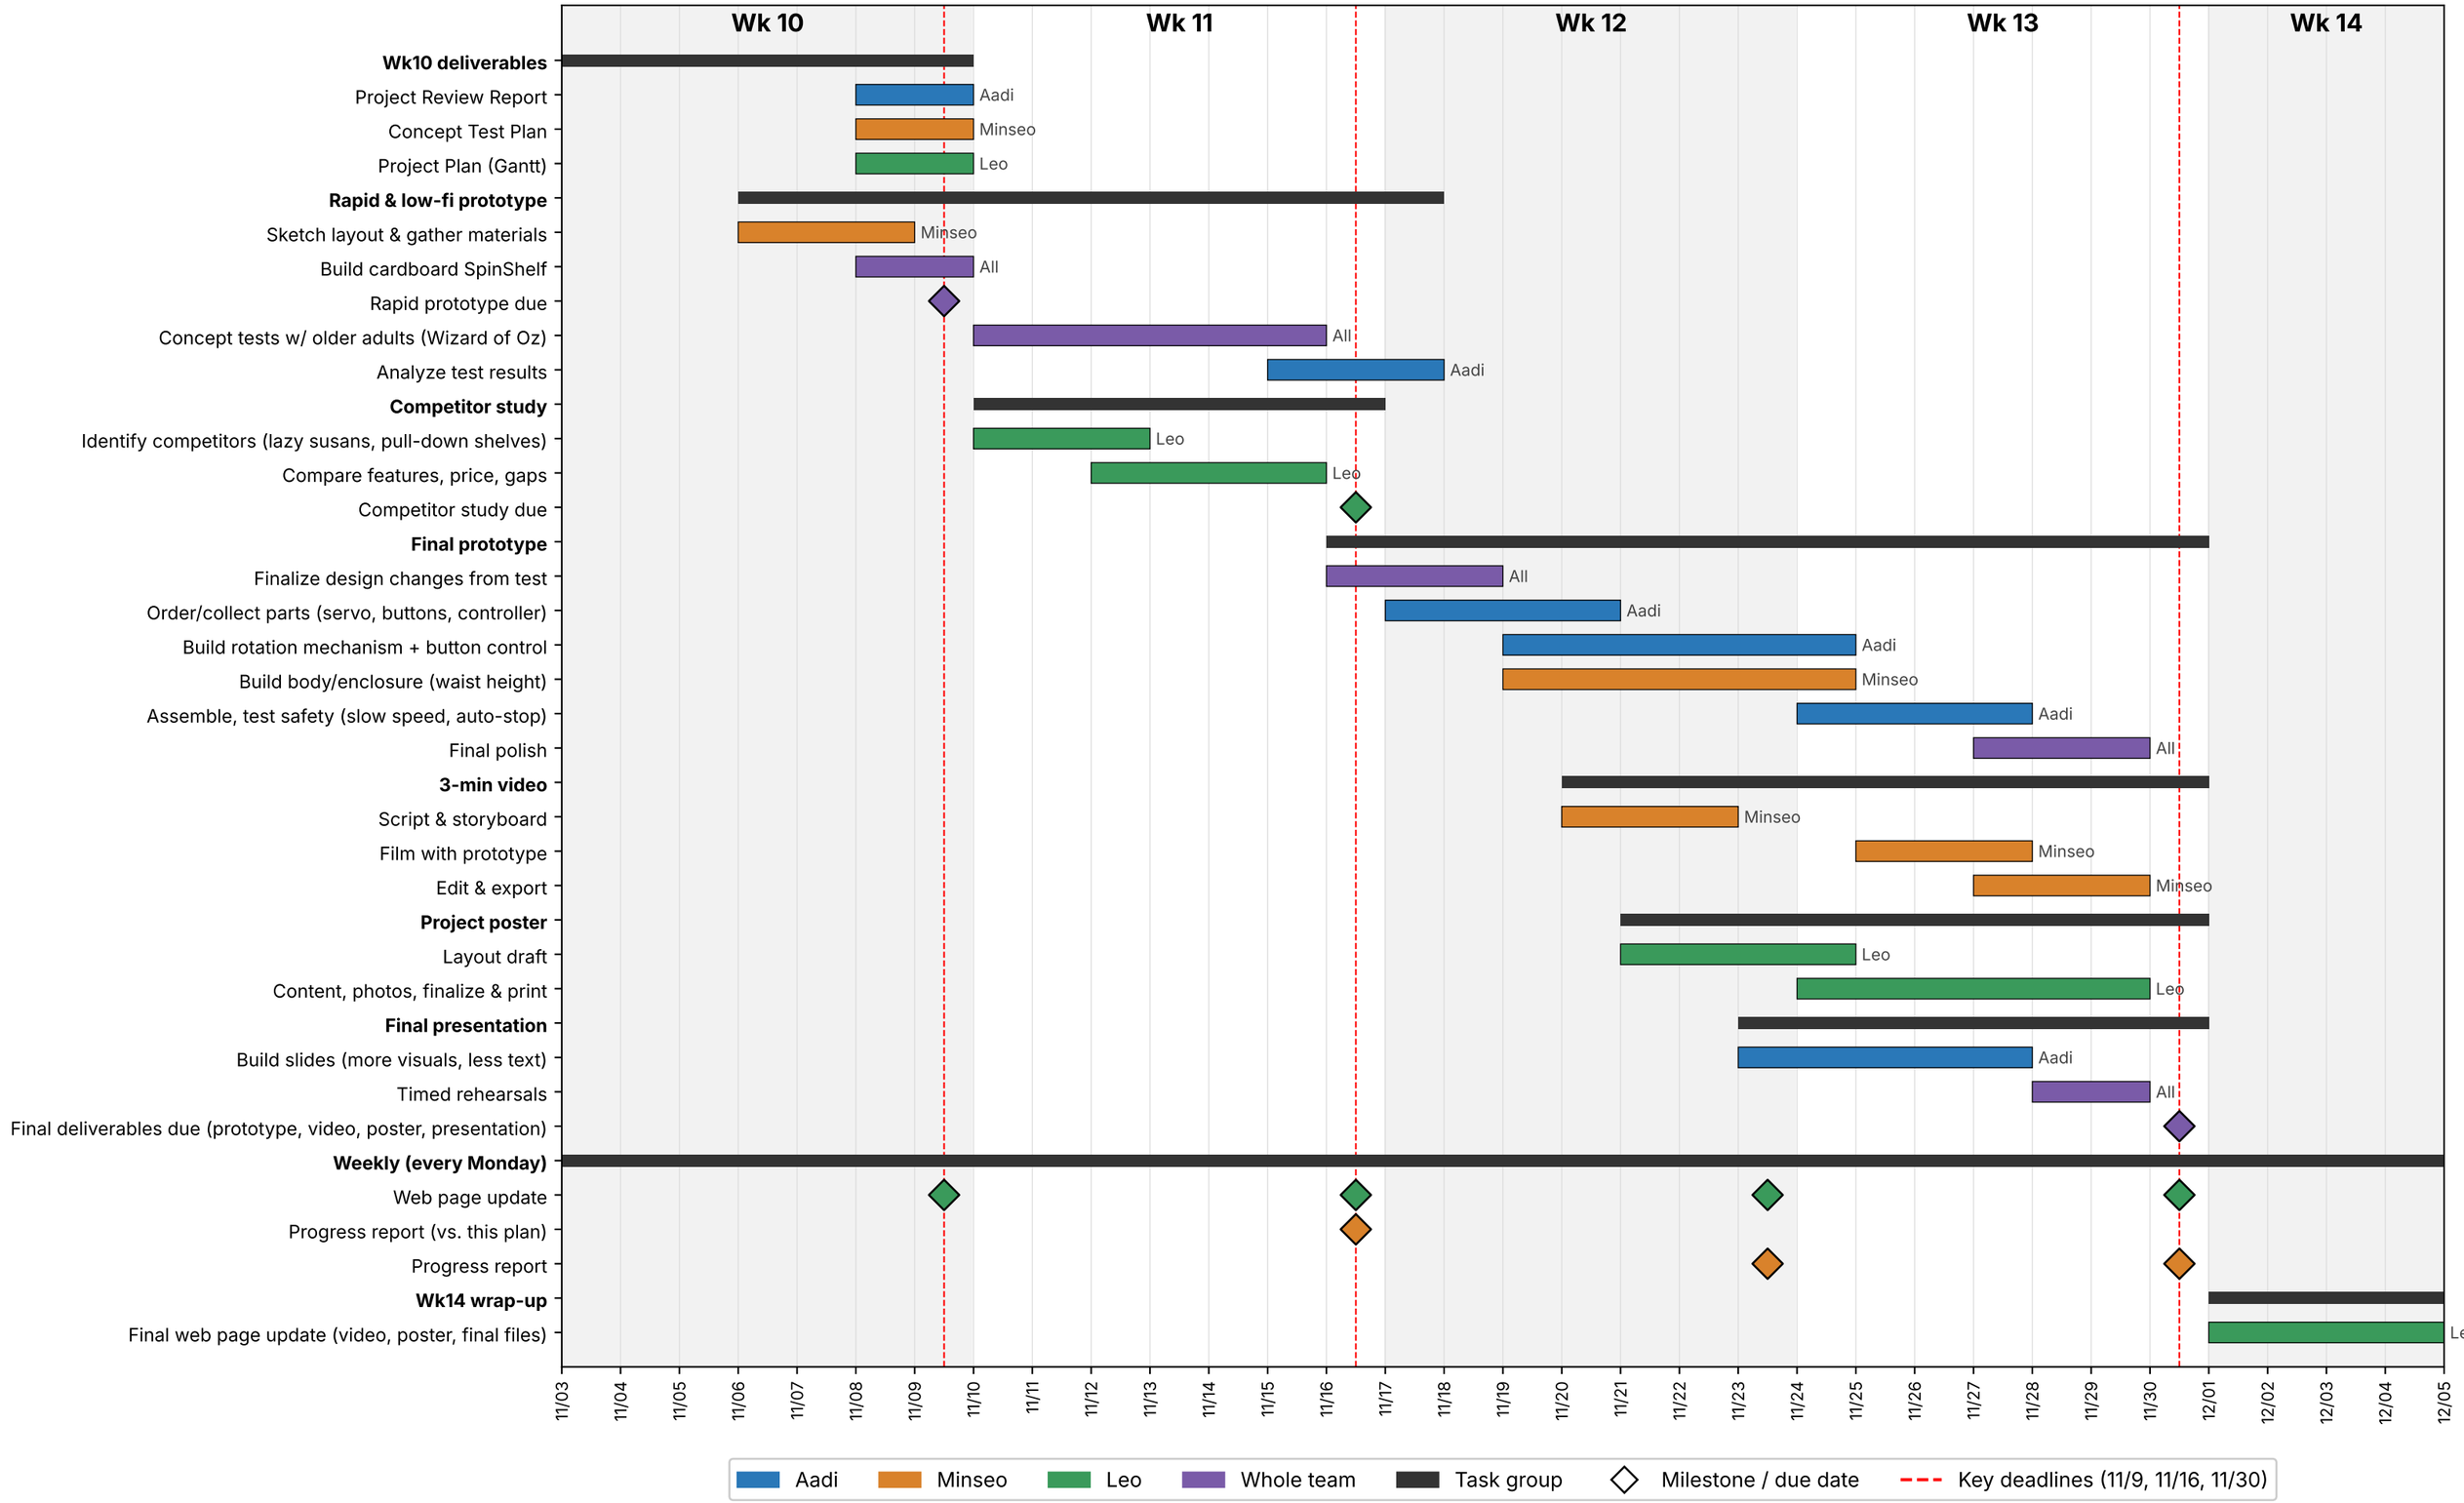

Task List: Owners, Dates, Dependencies

Task	Owner	Start	Due	Depends on
Wk10 deliverables				
Project Review Report	Aadi	Sun 11/08	Mon 11/09	Wk9 critique feedback
Concept Test Plan	Minseo	Sun 11/08	Mon 11/09	Prototype plan
Project Plan (Gantt)	Leo	Sun 11/08	Mon 11/09	Team task list
Rapid & low-fi prototype				
Sketch layout & gather materials	Minseo	Fri 11/06	Sun 11/08	Wk9 concept
Build cardboard SpinShelf	Whole team	Sun 11/08	Mon 11/09	Materials
Rapid prototype due	Whole team	Mon 11/09	Milestone	
Concept tests w/ older adults (Wizard of Oz)	Whole team	Tue 11/10	Sun 11/15	Prototype, Test Plan
Analyze test results	Aadi	Sun 11/15	Tue 11/17	Concept tests
Competitor study				
Identify competitors (lazy susans, pull-down shelves)	Leo	Tue 11/10	Thu 11/12	
Compare features, price, gaps	Leo	Thu 11/12	Sun 11/15	Competitor list
Competitor study due	Leo	Mon 11/16	Milestone	
Final prototype				
Finalize design changes from test	Whole team	Mon 11/16	Wed 11/18	Test results
Order/collect parts (servo, buttons, controller)	Aadi	Tue 11/17	Fri 11/20	Final design
Build rotation mechanism + button control	Aadi	Thu 11/19	Tue 11/24	Parts
Build body/enclosure (waist height)	Minseo	Thu 11/19	Tue 11/24	Final design
Assemble, test safety (slow speed, auto-stop)	Aadi	Tue 11/24	Fri 11/27	Mechanism, body
Final polish	Whole team	Fri 11/27	Sun 11/29	Assembly
3-min video				
Script & storyboard	Minseo	Fri 11/20	Sun 11/22	Final design
Film with prototype	Minseo	Wed 11/25	Fri 11/27	Working prototype
Edit & export	Minseo	Fri 11/27	Sun 11/29	Footage
Project poster				
Layout draft	Leo	Sat 11/21	Tue 11/24	Final design
Content, photos, finalize & print	Leo	Tue 11/24	Sun 11/29	Prototype photos
Final presentation				
Build slides (more visuals, less text)	Aadi	Mon 11/23	Fri 11/27	Test results, prototype
Timed rehearsals	Whole team	Sat 11/28	Sun 11/29	Slides
Final deliverables due (prototype, video, poster, presentation)	Whole team	Mon 11/30	Milestone	
Weekly (every Monday)				
Web page update	Leo	Mon 11/09	Milestone	That week's work
Web page update	Leo	Mon 11/16	Milestone	
Web page update	Leo	Mon 11/23	Milestone	
Web page update	Leo	Mon 11/30	Milestone	
Progress report (vs. this plan)	Minseo	Mon 11/16	Milestone	This plan
Progress report	Minseo	Mon 11/23	Milestone	
Progress report	Minseo	Mon 11/30	Milestone	
Wk14 wrap-up				
Final web page update (video, poster, final files)	Leo	Tue 12/01	Fri 12/04	Final deliverables
